LEVELOG

Blueview Construction

588 Thomas S Boyland St

588 Thomas S Boyland St, Brooklyn, NY

CONSTRUCTION PROGRESS REPORT

Oct 2–15, 2026


Prepared October 15, 2026 · Source: Levelog records — check-ins, daily logs and their photos, group chat

Summary

Work this period at 588 Thomas S Boyland: framing fl 1–4 (Arkon Builders), riser install fl 1–3 (Quality Plumbing), electrical rough-in fl 1–2 (Power Direct) and scaffolding (J&G Scaffolding). The site was worked 10 of 10 working days, with an average of 25 workers on site a day; the busiest day was Thu Oct 15 with 37. The daily log of Oct 6 notes: Concrete delivery for stair 2 pushed to next week by the supplier. 1 new DOB/DOT record was issued for the job (DOT permit X01-2026278-A11). 4 commitments are past due and 47 punch items remain open. Coming up: riser photos for the inspector from Quality Plumbing due Mon Oct 19 and Plumbing inspection, risers fl 1-3 (DOB) on Tue Oct 20.

10 of 10	25 avg	37 · Oct 15	4
Days on site	Workers on site / day	Busiest day	Subs on site

Actual work (from daily logs)

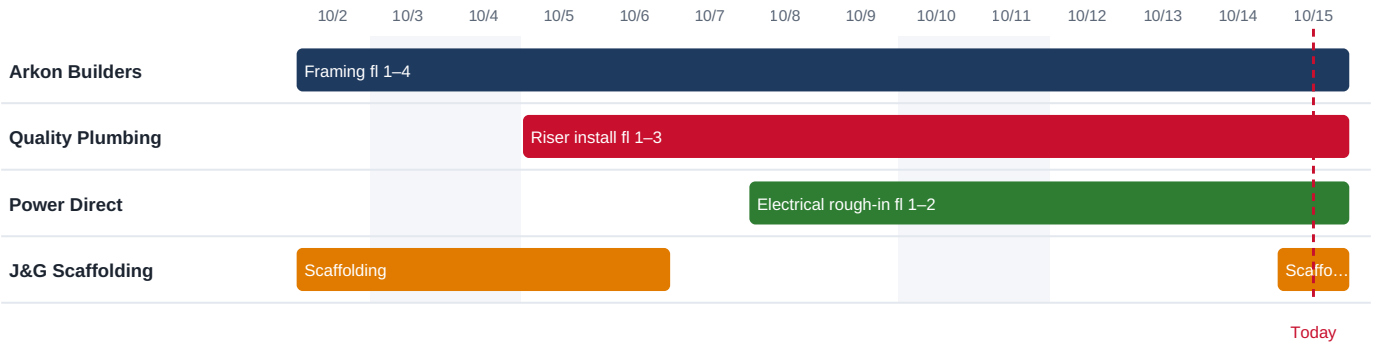

Bars are the days each sub was on site (check-ins); labels are the work written in the daily logs. No planned dates — no schedule is on file.

Work by sub

Arkon Builders — Framing

10 days on site · Oct 2–15 · avg 14.4, most 16 workers

- Framing — fl 1–2 (Oct 2–9)
- Framing — fl 3–4 (Oct 12–15)

Issues

- Late: Fire-blocking at the shaft walls, 2nd floor (due Oct 13)

Quality Plumbing — Plumbing

9 days on site · Oct 5–15 · avg 5.2, most 6 workers

- Riser install — fl 1–3 (Oct 5–15)

Issues

- Late: Pressure test risers fl 1-3 (due Oct 12)

Power Direct — Electrical

6 days on site · Oct 8–15 · avg 6.8, most 8 workers

- Electrical rough-in — fl 1–2 (Oct 8–15)

Issues

- Late: Send revised electrical shop drawings (due Oct 9)
- Oct 9: Power Direct short 2 workers today; rough-in on the 2nd floor behind.

J&G Scaffolding — Scaffolding

4 days on site · Oct 2–15 · avg 4.5, most 7 workers

- Scaffolding — Front facade (Oct 2–6)
- Scaffolding — Rear facade (Oct 15)


Issues

- Late: Netting on the front scaffold (due Oct 8)


Progress photos

From the daily logs: each photo dated, with the sub's work that day.


Arkon Builders



Fri Oct 2 Earliest
Framing — fl 1–2




Fri Oct 9
Framing — fl 1–2




Thu Oct 15 Latest
Framing — fl 3–4

J&G Scaffolding




Fri Oct 2 Earliest
Scaffolding — Front facade




Thu Oct 15 Latest
Scaffolding — Rear facade

Power Direct




Thu Oct 8 Earliest
Electrical rough-in — fl 1–2




Thu Oct 15 Latest
Electrical rough-in — fl 1–2

Quality Plumbing




Mon Oct 5 Earliest
Riser install — fl 1–3



Wed Oct 14 Latest
Riser install — fl 1–3

Site activity

Workers on site per day

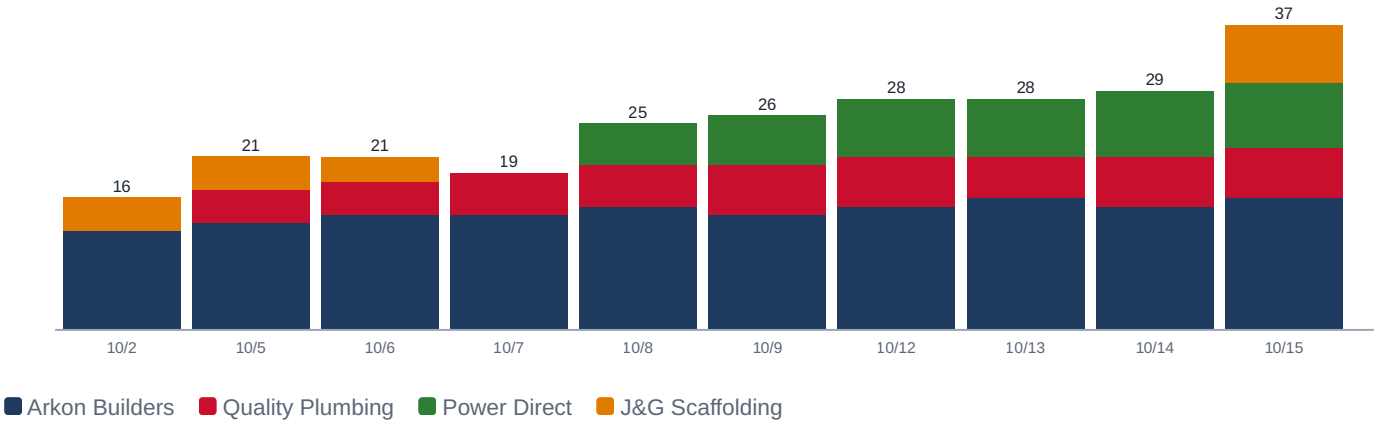

Worked 10 of 10 working days · average 25 workers on site a day · busiest Thu Oct 15 (37).

Sub	Days on site	Avg workers	Most workers
Arkon Builders	10	14.4	16
Quality Plumbing	9	5.2	6
Power Direct	6	6.8	8
J&G Scaffolding	4	4.5	7

Each worker counted once a day, from site check-ins.

DOB / DOT

Type	Number	Date	Status
DOT permit	X01-2026278-A11	Oct 8	ISSUED

Open items

Late commitments

Who	What	Due	Since
J&G Scaffolding	Netting on the front scaffold	Oct 8 (7 days late)	Oct 5
Power Direct	Send revised electrical shop drawings	Oct 9 (6 days late)	Oct 5
Quality Plumbing	Pressure test risers fl 1-3	Oct 12 (3 days late)	Oct 6
Arkon Builders	Fire-blocking at the shaft walls, 2nd floor	Oct 13 (2 days late)	Oct 8

Punch list

47 open · 0 ready to check · 0 closed.

Assigned to	Open	Ready to check	Closed
Unassigned	47	0	0

Coming up (next 2 weeks)

- **Mon Oct 19** — Quality Plumbing: Riser photos for the inspector (due)
- **Tue Oct 20** 9:00 AM — Plumbing inspection, risers fl 1-3 (DOB)
- **Fri Oct 23** — Concrete delivery for stair 2
